

PROJECT INFORMATION REPORT

City of Los Angeles

Bureau of Engineering


Department of Public Works

SSRP H30A Hollywood Fwy & Vine

(C757)

Current Phase	Scope of Work									
Construction	Based on Secondary Sewer Plan report H30 produced by Bureau of Sanitation in August 2005, this Project will Remove and Replace (R/R) or Rehabilitate approximately 3.94 -miles of sewer pipes as part of the Secondary Sewer Renewal Program 60 Miles Sewer Rehabilitation and Replacement Project of the Settlement Agreement Program. The project is located in Central area in an area bounded by Belden Dr. on the north, Beachwood Dr. on the east, Highland Ave. on the west, and Hollywood Blvd. on the south									
Construction Information										
Expected Duration: from 2/29/2008 to 1/16/2010 Construction Cost: \$4,129,881 Contractor: DLSB, Inc.										
Program Information										
Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Richard Pedrozo PM Phone: (213) 485-1638 Lead Division: WW Conveyance Engineering Work Order: SZC11620 (Active)	<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr style="background-color: #e6f2ff;"> <th style="width: 40%;">Council District(s)</th> <th style="width: 60%;">Project Status</th> </tr> </thead> <tbody> <tr> <td>4 - Tom LaBonge, 13 - Eric Garcetti</td> <td rowspan="4">Notice to proceed was issued on 4/7/08. The project is 85 percent complete. Construction completion may occur by 12/31/09.</td> </tr> <tr style="background-color: #e6f2ff;"> <th>Neighborhood Council(s)</th> </tr> <tr> <td>Hollywood Hills West NC, Hollywood United NC</td> </tr> <tr style="background-color: #e6f2ff;"> <th>Geographic Information</th> </tr> <tr> <td>Thomas Guide: 593-F3 Planning Area: Central Area Address: HOLLYWOOD FRWY & VINE</td> <td></td> </tr> </tbody> </table>	Council District(s)	Project Status	4 - Tom LaBonge, 13 - Eric Garcetti	Notice to proceed was issued on 4/7/08. The project is 85 percent complete. Construction completion may occur by 12/31/09.	Neighborhood Council(s)	Hollywood Hills West NC, Hollywood United NC	Geographic Information	Thomas Guide: 593-F3 Planning Area: Central Area Address: HOLLYWOOD FRWY & VINE	
Council District(s)		Project Status								
4 - Tom LaBonge, 13 - Eric Garcetti		Notice to proceed was issued on 4/7/08. The project is 85 percent complete. Construction completion may occur by 12/31/09.								
Neighborhood Council(s)										
Hollywood Hills West NC, Hollywood United NC										
Geographic Information										
Thomas Guide: 593-F3 Planning Area: Central Area Address: HOLLYWOOD FRWY & VINE										
Council District(s)										
4 - Tom LaBonge, 13 - Eric Garcetti										
Neighborhood Council(s)										
Hollywood Hills West NC, Hollywood United NC										
Geographic Information										
Thomas Guide: 593-F3 Planning Area: Central Area Address: HOLLYWOOD FRWY & VINE										

Information Resources
Listed below are various resources available for finding more information related to projects.
City of Los Angeles Internet Home Page
http://www.lacity.org/
Bureau of Engineering Internet Home Page
http://eng.lacity.org/
BOE Mapping Application (Navigate LA)
http://navigatela.lacity.org/
BOE Public Right of Way Reservation System
http://navigatela.lacity.org/pwrsview/
Bureau of Engineering Project Information Reports
http://eng.lacity.org/iuprs/
Bureau of Engineering Projects Out to Bid
http://eng.lacity.org/docs/dpw/bids/consbids.pdf

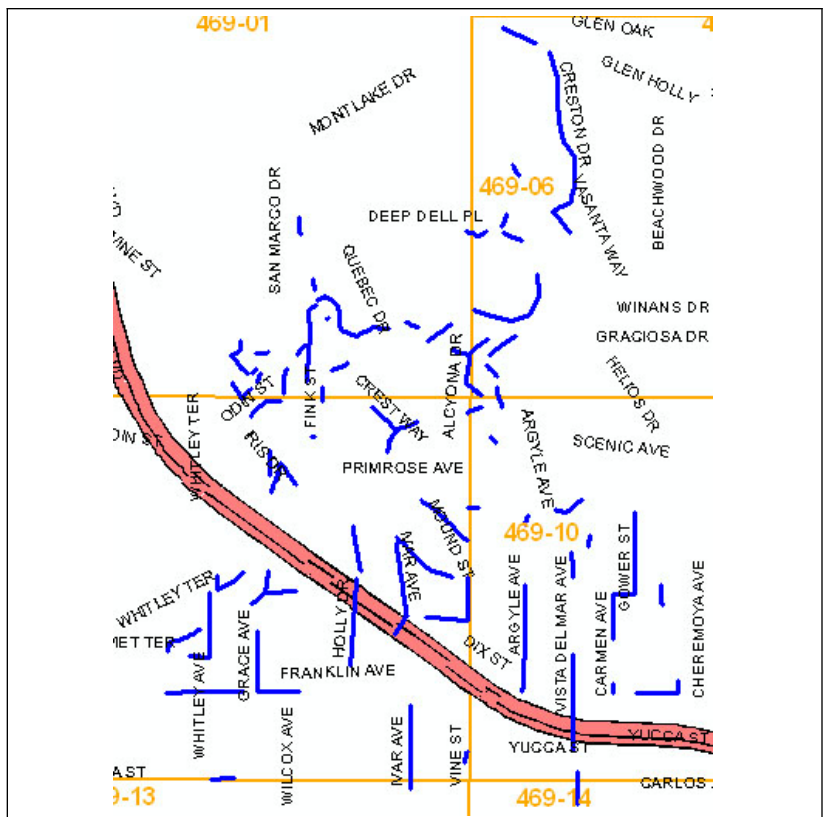

Gary Lee Moore, P.E.
City Engineer
