

# PROJECT INFORMATION REPORT

City of Los Angeles

Bureau of Engineering


Department of Public Works

## SSRP A02A Venice Blvd. & Genesee

(C764)

<table border="1"> <tr> <th style="text-align: center;">Current Phase</th> </tr> <tr> <td>Post-Construction</td> </tr> <tr> <th style="text-align: center;">Construction Information</th> </tr> <tr> <td>Expected Duration: from 4/28/2008 to 8/19/2009 Construction Cost: \$2,135,975 Contractor: Vasilj, Inc</td> </tr> <tr> <th style="text-align: center;">Program Information</th> </tr> <tr> <td>Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Richard Pedrozo PM Phone: (213) 485-1638 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11669 (Active)</td> </tr> <tr> <th style="text-align: center;">Council District(s)</th> </tr> <tr> <td>8 - Bernard C. Parks, 10 - Herb J. Wesson, Jr.</td> </tr> <tr> <th style="text-align: center;">Neighborhood Council(s)</th> </tr> <tr> <td>Empowerment Congress West Area NDC, Mid City NC, P.I.C.O. NC, South Robertson NC, West Adams</td> </tr> <tr> <th style="text-align: center;">Geographic Information</th> </tr> <tr> <td>Thomas Guide: 633, 673 Planning Area: South Area Address: Venice Blvd. &amp; Genesee</td> </tr> </table>	Current Phase	Post-Construction	Construction Information	Expected Duration: from 4/28/2008 to 8/19/2009 Construction Cost: \$2,135,975 Contractor: Vasilj, Inc	Program Information	Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Richard Pedrozo PM Phone: (213) 485-1638 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11669 (Active)	Council District(s)	8 - Bernard C. Parks, 10 - Herb J. Wesson, Jr.	Neighborhood Council(s)	Empowerment Congress West Area NDC, Mid City NC, P.I.C.O. NC, South Robertson NC, West Adams	Geographic Information	Thomas Guide: 633, 673 Planning Area: South Area Address: Venice Blvd. & Genesee	<table border="1"> <tr> <th style="text-align: center;">Scope of Work</th> </tr> <tr> <td>Based on Secondary Sewer Plan report A02 received from Bureau of Sanitation in August 2005, this Project will Remove and Replace (R/R) or Rehabilitate approximately 3.45 -miles of sewer pipes as part of the Secondary Sewer Renewal Program 60 Miles Sewer Rehabilitation and Replacement of the Settlement Agreement Program. The project is located in South Los Angeles and Central in an area bounded by Pico Bl. on the north Redondo Bl. on the east, Robertson Bl. on the west, and Stocker St. on the south.</td> </tr> <tr> <th style="text-align: center;">Project Status</th> </tr> <tr> <td>The design of this project was completed in July 2007 and was advertised for construction in December 2007. Bids were opened on January 9, 2008 and on March 21, 2008 the project was awarded to Vasilj Construction in the amount of \$1,941,795.50. The project consists of replacing or lining various deteriorated sewers in Council Districts 8 and 10. Construction began on May 20, 2008 and rehabilitation of the last sewer reach was completed on July 13, 2009. Final inspection of the project was performed on 8/12/09.</td> </tr> </table>	Scope of Work	Based on Secondary Sewer Plan report A02 received from Bureau of Sanitation in August 2005, this Project will Remove and Replace (R/R) or Rehabilitate approximately 3.45 -miles of sewer pipes as part of the Secondary Sewer Renewal Program 60 Miles Sewer Rehabilitation and Replacement of the Settlement Agreement Program. The project is located in South Los Angeles and Central in an area bounded by Pico Bl. on the north Redondo Bl. on the east, Robertson Bl. on the west, and Stocker St. on the south.	Project Status	The design of this project was completed in July 2007 and was advertised for construction in December 2007. Bids were opened on January 9, 2008 and on March 21, 2008 the project was awarded to Vasilj Construction in the amount of \$1,941,795.50. The project consists of replacing or lining various deteriorated sewers in Council Districts 8 and 10. Construction began on May 20, 2008 and rehabilitation of the last sewer reach was completed on July 13, 2009. Final inspection of the project was performed on 8/12/09.
Current Phase																	
Post-Construction																	
Construction Information																	
Expected Duration: from 4/28/2008 to 8/19/2009 Construction Cost: \$2,135,975 Contractor: Vasilj, Inc																	
Program Information																	
Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Richard Pedrozo PM Phone: (213) 485-1638 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11669 (Active)																	
Council District(s)																	
8 - Bernard C. Parks, 10 - Herb J. Wesson, Jr.																	
Neighborhood Council(s)																	
Empowerment Congress West Area NDC, Mid City NC, P.I.C.O. NC, South Robertson NC, West Adams																	
Geographic Information																	
Thomas Guide: 633, 673 Planning Area: South Area Address: Venice Blvd. & Genesee																	
Scope of Work																	
Based on Secondary Sewer Plan report A02 received from Bureau of Sanitation in August 2005, this Project will Remove and Replace (R/R) or Rehabilitate approximately 3.45 -miles of sewer pipes as part of the Secondary Sewer Renewal Program 60 Miles Sewer Rehabilitation and Replacement of the Settlement Agreement Program. The project is located in South Los Angeles and Central in an area bounded by Pico Bl. on the north Redondo Bl. on the east, Robertson Bl. on the west, and Stocker St. on the south.																	
Project Status																	
The design of this project was completed in July 2007 and was advertised for construction in December 2007. Bids were opened on January 9, 2008 and on March 21, 2008 the project was awarded to Vasilj Construction in the amount of \$1,941,795.50. The project consists of replacing or lining various deteriorated sewers in Council Districts 8 and 10. Construction began on May 20, 2008 and rehabilitation of the last sewer reach was completed on July 13, 2009. Final inspection of the project was performed on 8/12/09.																	

Information Resources
Listed below are various resources available for finding more information related to projects.
City of Los Angeles Internet Home Page <a href="http://www.lacity.org/">http://www.lacity.org/</a>
Bureau of Engineering Internet Home Page <a href="http://eng.lacity.org/">http://eng.lacity.org/</a>
BOE Mapping Application (Navigate LA) <a href="http://navigatela.lacity.org/">http://navigatela.lacity.org/</a>
BOE Public Right of Way Reservation System <a href="http://navigatela.lacity.org/pwrsview/">http://navigatela.lacity.org/pwrsview/</a>
Bureau of Engineering Project Information Reports <a href="http://eng.lacity.org/iuprs/">http://eng.lacity.org/iuprs/</a>
Bureau of Engineering Projects Out to Bid <a href="http://eng.lacity.org/docs/dpw/bids/consbids.pdf">http://eng.lacity.org/docs/dpw/bids/consbids.pdf</a>

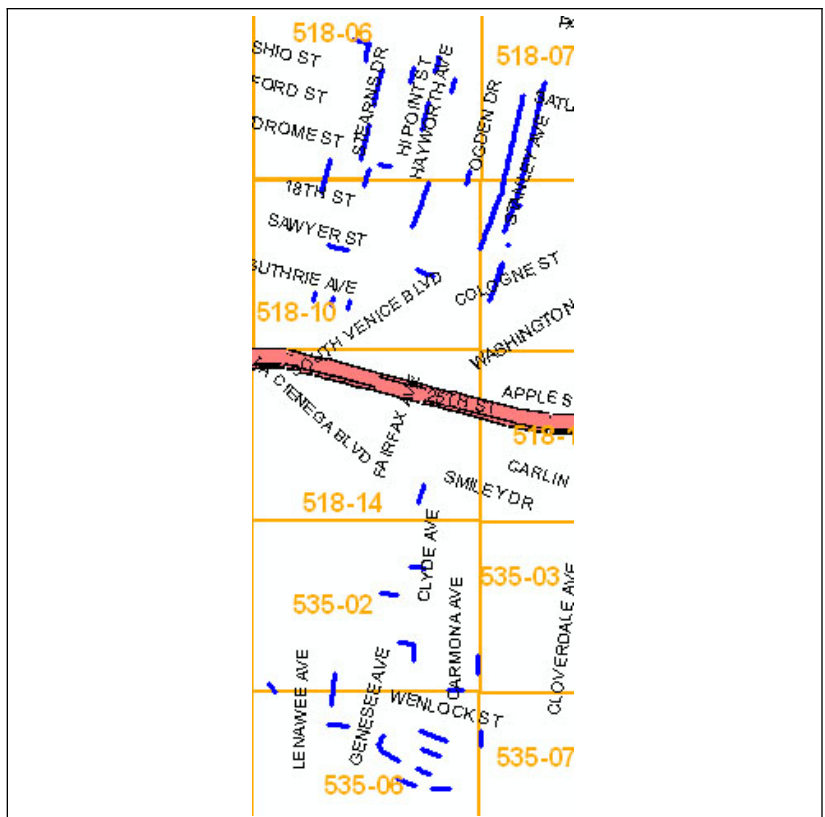

Gary Lee Moore, P.E.  
City Engineer
