

# PROJECT INFORMATION REPORT

City of Los Angeles


Bureau of Engineering

Department of Public Works

## Odor Control Hollydale Drive Local Sewer Addition (C766)

<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="background-color: #e6f2ff;">Current Phase</th> </tr> <tr> <td>Post-Construction</td> </tr> <tr> <th style="background-color: #e6f2ff;">Construction Information</th> </tr> <tr> <td>Expected Duration: from 8/1/2008 to 3/29/2010 Construction Cost: \$1,071,180 Contractor: Ramona Inc.</td> </tr> <tr> <th style="background-color: #e6f2ff;">Program Information</th> </tr> <tr> <td>Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Sean Zahedi PM Phone: (213) 847-0402 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11697 (Active)</td> </tr> <tr> <th style="background-color: #e6f2ff;">Council District(s)</th> </tr> <tr> <td>13 - Eric Garcetti</td> </tr> <tr> <th style="background-color: #e6f2ff;">Neighborhood Council(s)</th> </tr> <tr> <td>Atwater Village NC</td> </tr> <tr> <th style="background-color: #e6f2ff;">Geographic Information</th> </tr> <tr> <td>Thomas Guide: 594 D2 Planning Area: East Area Address: N/A</td> </tr> </table>	Current Phase	Post-Construction	Construction Information	Expected Duration: from 8/1/2008 to 3/29/2010 Construction Cost: \$1,071,180 Contractor: Ramona Inc.	Program Information	Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Sean Zahedi PM Phone: (213) 847-0402 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11697 (Active)	Council District(s)	13 - Eric Garcetti	Neighborhood Council(s)	Atwater Village NC	Geographic Information	Thomas Guide: 594 D2 Planning Area: East Area Address: N/A	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="background-color: #e6f2ff;">Scope of Work</th> </tr> <tr> <td>This project will build approximately 3,100 feet of 8-inch diameter sewer in Hollydale Drive between Glendale Blvd and Silverlake Blvd, parallel to the existing 42-inch diameter North Outfall Sewer (NOS). Approximately 80 house connections along this alignment will be re-connected to the new 8-inch line. Existing 8" sewers adjacent to the new sewer will be retrofitted with trap maintenance holes or will be reconnected to the new sewer.</td> </tr> <tr> <th style="background-color: #e6f2ff;">Project Status</th> </tr> <tr> <td>Notice to proceed was issued on September 3, 2008. Construction is 100% complete.</td> </tr> </table>	Scope of Work	This project will build approximately 3,100 feet of 8-inch diameter sewer in Hollydale Drive between Glendale Blvd and Silverlake Blvd, parallel to the existing 42-inch diameter North Outfall Sewer (NOS). Approximately 80 house connections along this alignment will be re-connected to the new 8-inch line. Existing 8" sewers adjacent to the new sewer will be retrofitted with trap maintenance holes or will be reconnected to the new sewer.	Project Status	Notice to proceed was issued on September 3, 2008. Construction is 100% complete.
Current Phase																	
Post-Construction																	
Construction Information																	
Expected Duration: from 8/1/2008 to 3/29/2010 Construction Cost: \$1,071,180 Contractor: Ramona Inc.																	
Program Information																	
Program: Wastewater Collection System Settlement Agreement - 60 Miles Project Mgr: Sean Zahedi PM Phone: (213) 847-0402 Lead Division: Wastewater Conveyance Engineering Work Order: SZC11697 (Active)																	
Council District(s)																	
13 - Eric Garcetti																	
Neighborhood Council(s)																	
Atwater Village NC																	
Geographic Information																	
Thomas Guide: 594 D2 Planning Area: East Area Address: N/A																	
Scope of Work																	
This project will build approximately 3,100 feet of 8-inch diameter sewer in Hollydale Drive between Glendale Blvd and Silverlake Blvd, parallel to the existing 42-inch diameter North Outfall Sewer (NOS). Approximately 80 house connections along this alignment will be re-connected to the new 8-inch line. Existing 8" sewers adjacent to the new sewer will be retrofitted with trap maintenance holes or will be reconnected to the new sewer.																	
Project Status																	
Notice to proceed was issued on September 3, 2008. Construction is 100% complete.																	

Information Resources												
Listed below are various resources available for finding more information related to projects.												
<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="background-color: #e6f2ff;">City of Los Angeles Internet Home Page</th> </tr> <tr> <td><a href="http://www.lacity.org/">http://www.lacity.org/</a></td> </tr> <tr> <th style="background-color: #e6f2ff;">Bureau of Engineering Internet Home Page</th> </tr> <tr> <td><a href="http://eng.lacity.org/">http://eng.lacity.org/</a></td> </tr> <tr> <th style="background-color: #e6f2ff;">BOE Mapping Application (Navigate LA)</th> </tr> <tr> <td><a href="http://navigatela.lacity.org/">http://navigatela.lacity.org/</a></td> </tr> <tr> <th style="background-color: #e6f2ff;">BOE Public Right of Way Reservation System</th> </tr> <tr> <td><a href="http://navigatela.lacity.org/pwrsview/">http://navigatela.lacity.org/pwrsview/</a></td> </tr> <tr> <th style="background-color: #e6f2ff;">Bureau of Engineering Project Information Reports</th> </tr> <tr> <td><a href="http://eng.lacity.org/iuprs/">http://eng.lacity.org/iuprs/</a></td> </tr> <tr> <th style="background-color: #e6f2ff;">Bureau of Engineering Projects Out to Bid</th> </tr> <tr> <td><a href="http://eng.lacity.org/docs/dpw/bids/consbids.pdf">http://eng.lacity.org/docs/dpw/bids/consbids.pdf</a></td> </tr> </table>	City of Los Angeles Internet Home Page	<a href="http://www.lacity.org/">http://www.lacity.org/</a>	Bureau of Engineering Internet Home Page	<a href="http://eng.lacity.org/">http://eng.lacity.org/</a>	BOE Mapping Application (Navigate LA)	<a href="http://navigatela.lacity.org/">http://navigatela.lacity.org/</a>	BOE Public Right of Way Reservation System	<a href="http://navigatela.lacity.org/pwrsview/">http://navigatela.lacity.org/pwrsview/</a>	Bureau of Engineering Project Information Reports	<a href="http://eng.lacity.org/iuprs/">http://eng.lacity.org/iuprs/</a>	Bureau of Engineering Projects Out to Bid	<a href="http://eng.lacity.org/docs/dpw/bids/consbids.pdf">http://eng.lacity.org/docs/dpw/bids/consbids.pdf</a>
City of Los Angeles Internet Home Page												
<a href="http://www.lacity.org/">http://www.lacity.org/</a>												
Bureau of Engineering Internet Home Page												
<a href="http://eng.lacity.org/">http://eng.lacity.org/</a>												
BOE Mapping Application (Navigate LA)												
<a href="http://navigatela.lacity.org/">http://navigatela.lacity.org/</a>												
BOE Public Right of Way Reservation System												
<a href="http://navigatela.lacity.org/pwrsview/">http://navigatela.lacity.org/pwrsview/</a>												
Bureau of Engineering Project Information Reports												
<a href="http://eng.lacity.org/iuprs/">http://eng.lacity.org/iuprs/</a>												
Bureau of Engineering Projects Out to Bid												
<a href="http://eng.lacity.org/docs/dpw/bids/consbids.pdf">http://eng.lacity.org/docs/dpw/bids/consbids.pdf</a>												

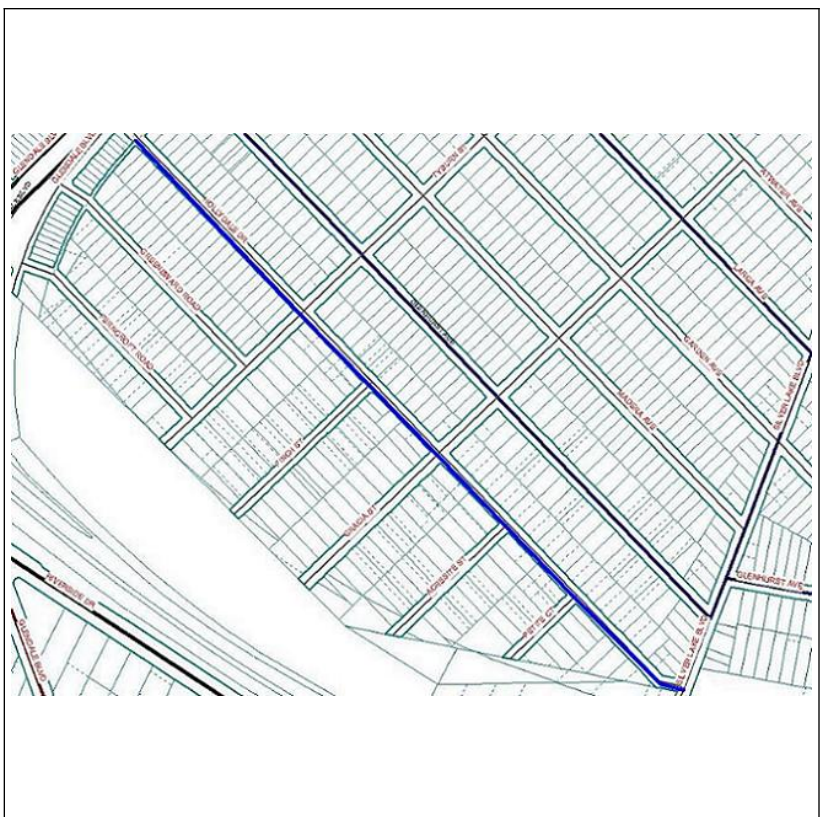

Gary Lee Moore, P.E.  
City Engineer
