

# PROJECT INFORMATION REPORT

City of Los Angeles

Bureau of Engineering


Department of Public Works

## Air Treatment Facility - NCOS

**(C476)**

<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="background-color: #e6f2ff;">Current Phase</th> </tr> <tr> <td>Construction</td> </tr> <tr> <th style="background-color: #e6f2ff;">Construction Information</th> </tr> <tr> <td>Expected Duration: from 6/29/2008 to 2/11/2011 Construction Cost: \$12,725,000 Contractor: Steve P. Rados, Inc.</td> </tr> <tr> <th style="background-color: #e6f2ff;">Program Information</th> </tr> <tr> <td>Program: Wastewater Collection System Settlement Agreement - Appendix Project Mgr: Gus Malkoun PM Phone: (213) 485-1646 Lead Division: WW Conveyance Engineering Work Order: SZC11286 (Active)</td> </tr> <tr> <th style="background-color: #e6f2ff;">Council District(s)</th> </tr> <tr> <td>10 - Herb J. Wesson, Jr.</td> </tr> <tr> <th style="background-color: #e6f2ff;">Neighborhood Council(s)</th> </tr> <tr> <td>Empowerment Congress West Area NDC</td> </tr> <tr> <th style="background-color: #e6f2ff;">Geographic Information</th> </tr> <tr> <td>Thomas Guide: 672J1 Planning Area: South Area Address: 6000 Jefferson Blvd, Los Angeles, CA 90016</td> </tr> </table>	Current Phase	Construction	Construction Information	Expected Duration: from 6/29/2008 to 2/11/2011 Construction Cost: \$12,725,000 Contractor: Steve P. Rados, Inc.	Program Information	Program: Wastewater Collection System Settlement Agreement - Appendix Project Mgr: Gus Malkoun PM Phone: (213) 485-1646 Lead Division: WW Conveyance Engineering Work Order: SZC11286 (Active)	Council District(s)	10 - Herb J. Wesson, Jr.	Neighborhood Council(s)	Empowerment Congress West Area NDC	Geographic Information	Thomas Guide: 672J1 Planning Area: South Area Address: 6000 Jefferson Blvd, Los Angeles, CA 90016	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="background-color: #e6f2ff;">Scope of Work</th> </tr> <tr> <td>This project includes the design and construction of the Bureau of Sanitation's Air Treatment Facility located at 6000 Jefferson Blvd. The facility is designed to ventilate a pressurized major sewer line in order to mitigate emission of sewer gas. The facility's two treatment stages will treat 12,000 cubic feet per minute of foul air by passing it through (1) biotrickling filters and (2) carbon adsorption units. The process will remove odorous compounds and volatile organics from the gas prior to its release into the atmosphere.</td> </tr> <tr> <th style="background-color: #e6f2ff;">Project Status</th> </tr> <tr> <td>Sep/10 by D.Copp Summary of Work Instrumentation and equipment testing &amp; calibration is ongoing. The odor control fans have been commissioned and appear to be working properly. Corrections to the property's drainage system via Change Order are ongoing. Valve dampers at the carbon units were replaced by the manufacturer due to excessive leakage. Landscape area has been cleaned and prepped for grading and landscaping. The community artist has installed three elements of her work on the North perimeter facade.</td> </tr> </table>	Scope of Work	This project includes the design and construction of the Bureau of Sanitation's Air Treatment Facility located at 6000 Jefferson Blvd. The facility is designed to ventilate a pressurized major sewer line in order to mitigate emission of sewer gas. The facility's two treatment stages will treat 12,000 cubic feet per minute of foul air by passing it through (1) biotrickling filters and (2) carbon adsorption units. The process will remove odorous compounds and volatile organics from the gas prior to its release into the atmosphere.	Project Status	Sep/10 by D.Copp Summary of Work Instrumentation and equipment testing & calibration is ongoing. The odor control fans have been commissioned and appear to be working properly. Corrections to the property's drainage system via Change Order are ongoing. Valve dampers at the carbon units were replaced by the manufacturer due to excessive leakage. Landscape area has been cleaned and prepped for grading and landscaping. The community artist has installed three elements of her work on the North perimeter facade.
Current Phase																	
Construction																	
Construction Information																	
Expected Duration: from 6/29/2008 to 2/11/2011 Construction Cost: \$12,725,000 Contractor: Steve P. Rados, Inc.																	
Program Information																	
Program: Wastewater Collection System Settlement Agreement - Appendix Project Mgr: Gus Malkoun PM Phone: (213) 485-1646 Lead Division: WW Conveyance Engineering Work Order: SZC11286 (Active)																	
Council District(s)																	
10 - Herb J. Wesson, Jr.																	
Neighborhood Council(s)																	
Empowerment Congress West Area NDC																	
Geographic Information																	
Thomas Guide: 672J1 Planning Area: South Area Address: 6000 Jefferson Blvd, Los Angeles, CA 90016																	
Scope of Work																	
This project includes the design and construction of the Bureau of Sanitation's Air Treatment Facility located at 6000 Jefferson Blvd. The facility is designed to ventilate a pressurized major sewer line in order to mitigate emission of sewer gas. The facility's two treatment stages will treat 12,000 cubic feet per minute of foul air by passing it through (1) biotrickling filters and (2) carbon adsorption units. The process will remove odorous compounds and volatile organics from the gas prior to its release into the atmosphere.																	
Project Status																	
Sep/10 by D.Copp Summary of Work Instrumentation and equipment testing & calibration is ongoing. The odor control fans have been commissioned and appear to be working properly. Corrections to the property's drainage system via Change Order are ongoing. Valve dampers at the carbon units were replaced by the manufacturer due to excessive leakage. Landscape area has been cleaned and prepped for grading and landscaping. The community artist has installed three elements of her work on the North perimeter facade.																	

Information Resources
Listed below are various resources available for finding more information related to projects.
City of Los Angeles Internet Home Page
<a href="http://www.lacity.org/">http://www.lacity.org/</a>
Bureau of Engineering Internet Home Page
<a href="http://eng.lacity.org/">http://eng.lacity.org/</a>
BOE Mapping Application (Navigate LA)
<a href="http://navigatela.lacity.org/">http://navigatela.lacity.org/</a>
BOE Public Right of Way Reservation System
<a href="http://navigatela.lacity.org/pwrsview/">http://navigatela.lacity.org/pwrsview/</a>
Bureau of Engineering Project Information Reports
<a href="http://eng.lacity.org/iuprs/">http://eng.lacity.org/iuprs/</a>
Bureau of Engineering Projects Out to Bid
<a href="http://eng.lacity.org/docs/dpw/bids/consbids.pdf">http://eng.lacity.org/docs/dpw/bids/consbids.pdf</a>

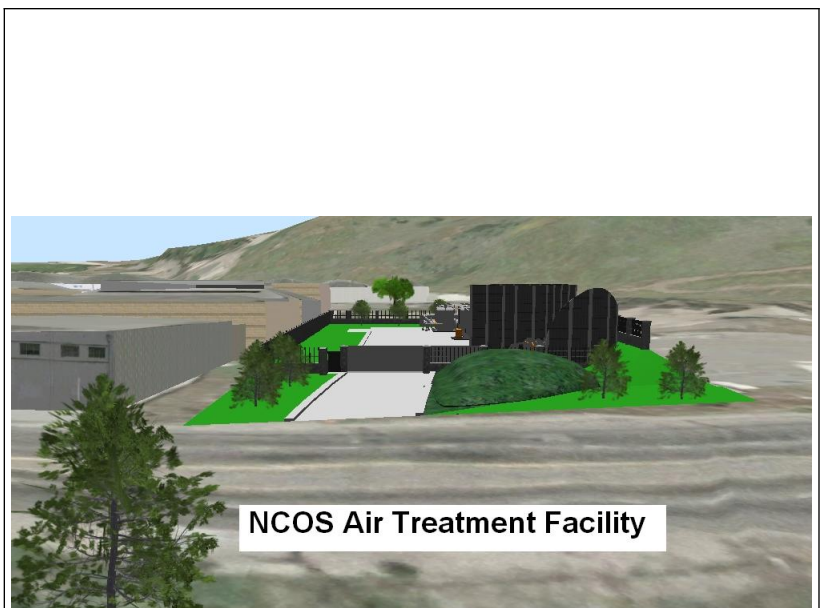

Gary Lee Moore, P.E.  
City Engineer
