PROJECT INFORMATION REPORT

City of Los Angeles | Bureau of Engineering | Department of Public Works

N. Broadway Swr Rehab. (C485)

Current Phase

Post-Construction

Construction Information

Expected Duration: from 6/8/2008 to 7/8/2009

Construction Cost: $1,304,453

Contractor: Insituform Technologies

Program Information

Program: Wastewater Collection System Settlement Agreement - 60 Miles

Project Mgr: Sean Zahedi

PM Phone: (213) 847-0402

Lead Division: Wastewater Conveyance Engineering

Work Order: SZC11521 (Active)

Scope of Work

This project proposes to rehabilitate 1,112 feet of structurally deteriorated 15" diameter clay pipe and 234 feet of 18" diameter clay pipe by the Cured-In-Place Pipe (CIPP) liner method. This project will also include a by-pass system, point repairs, installation of one (1) maintenance hole, rehabilitation of five (5) maintenance holes and traffic control. The project boundaries are N. Broadway between Bernard St. and College St. and Cesar Chavez Av. between N. Broadway and New High St.

Council District(s)

1 - Ed Reyes

Project Status

July/09

Summary of Work

All field works completed.

Neighborhood Council(s)

Downtown Los Angeles NC

Geographic Information

Thomas Guide: 634-G2,G3

Planning Area: Central Area

Address: N. Broadway btw Bernard St. and College St.

Information Resources

Listed below are various resources available for finding more information related to projects.

City of Los Angeles Internet Home Page	http://www.lacity.org/
Bureau of Engineering Internet Home Page	http://eng.lacity.org/
BOE Mapping Application (Navigate LA)	http://navigatela.lacity.org/
BOE Public Right of Way Reservation System	http://navigatela.lacity.org/pwrsview/
Bureau of Engineering Project Information Reports	http://eng.lacity.org/iuprs/
Bureau of Engineering Projects Out to Bid	http://eng.lacity.org/docs/dpw/bids/consbids.pdf

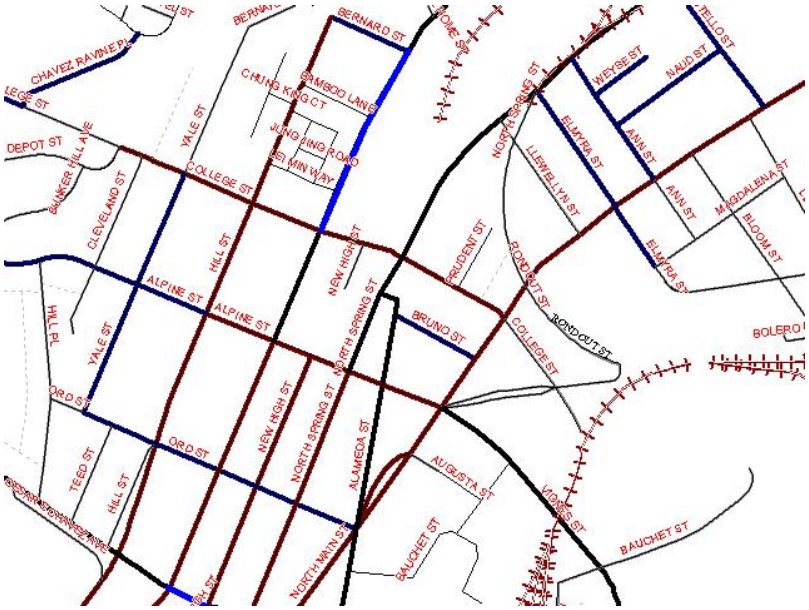

BUREAU OF ENGINEERING
SERVING THE PRESENT; DESIGNING FOR THE FUTURE

Gary Lee Moore, P.E.
City Engineer
